Activity Description	Planned (Months)	Start	Finish
San Diego CE			
Dist Serv Center/Renov & Land Aquisition			
Design - Passenger Elevator	28	06/10/04A	09/29/06A
DSA - Passenger Elevator	6	10/02/06A	01/31/07A
Construction - Passenger Elevator	6	02/01/07A	07/31/07A
Design - Maint./Warehouse Ren.	4	07/16/07A	10/31/07A
DSA - Maint./Warehouse Ren.	6	11/01/07A	04/30/08A
Bid & Award - Maint./Warehouse Ren.	3	05/01/08A	07/31/08
Construction - Maint./Warehouse Ren.	8	08/01/08	03/31/09
ECC- Land Acq. & Reloc. Skills Ctr.			
Design	12	02/02/04A	01/31/06A
DSA	6	01/30/06A	10/31/06A
Bid & Award	3	04/02/07A	06/29/07A
Demolition	3	04/02/07A	07/06/07A
Construction	15	07/09/07A	09/19/08
West City Campus			
Design	18	02/02/04A	09/30/05A
DSA	6	10/03/05A	11/30/06A
Bid & Award	3	04/02/07A	06/29/07A
Construction	21	08/01/07A	04/16/09
Clairemont/Linda Vista Campus - Land Acq and Bld			
Design	12	04/02/07A	12/31/08
Land Aquisition	7	05/01/07A	12/31/08
DSA	6	01/01/09	07/02/09
Bid & Award	3	07/03/09	10/01/09
Construction	12	10/02/09	09/30/10

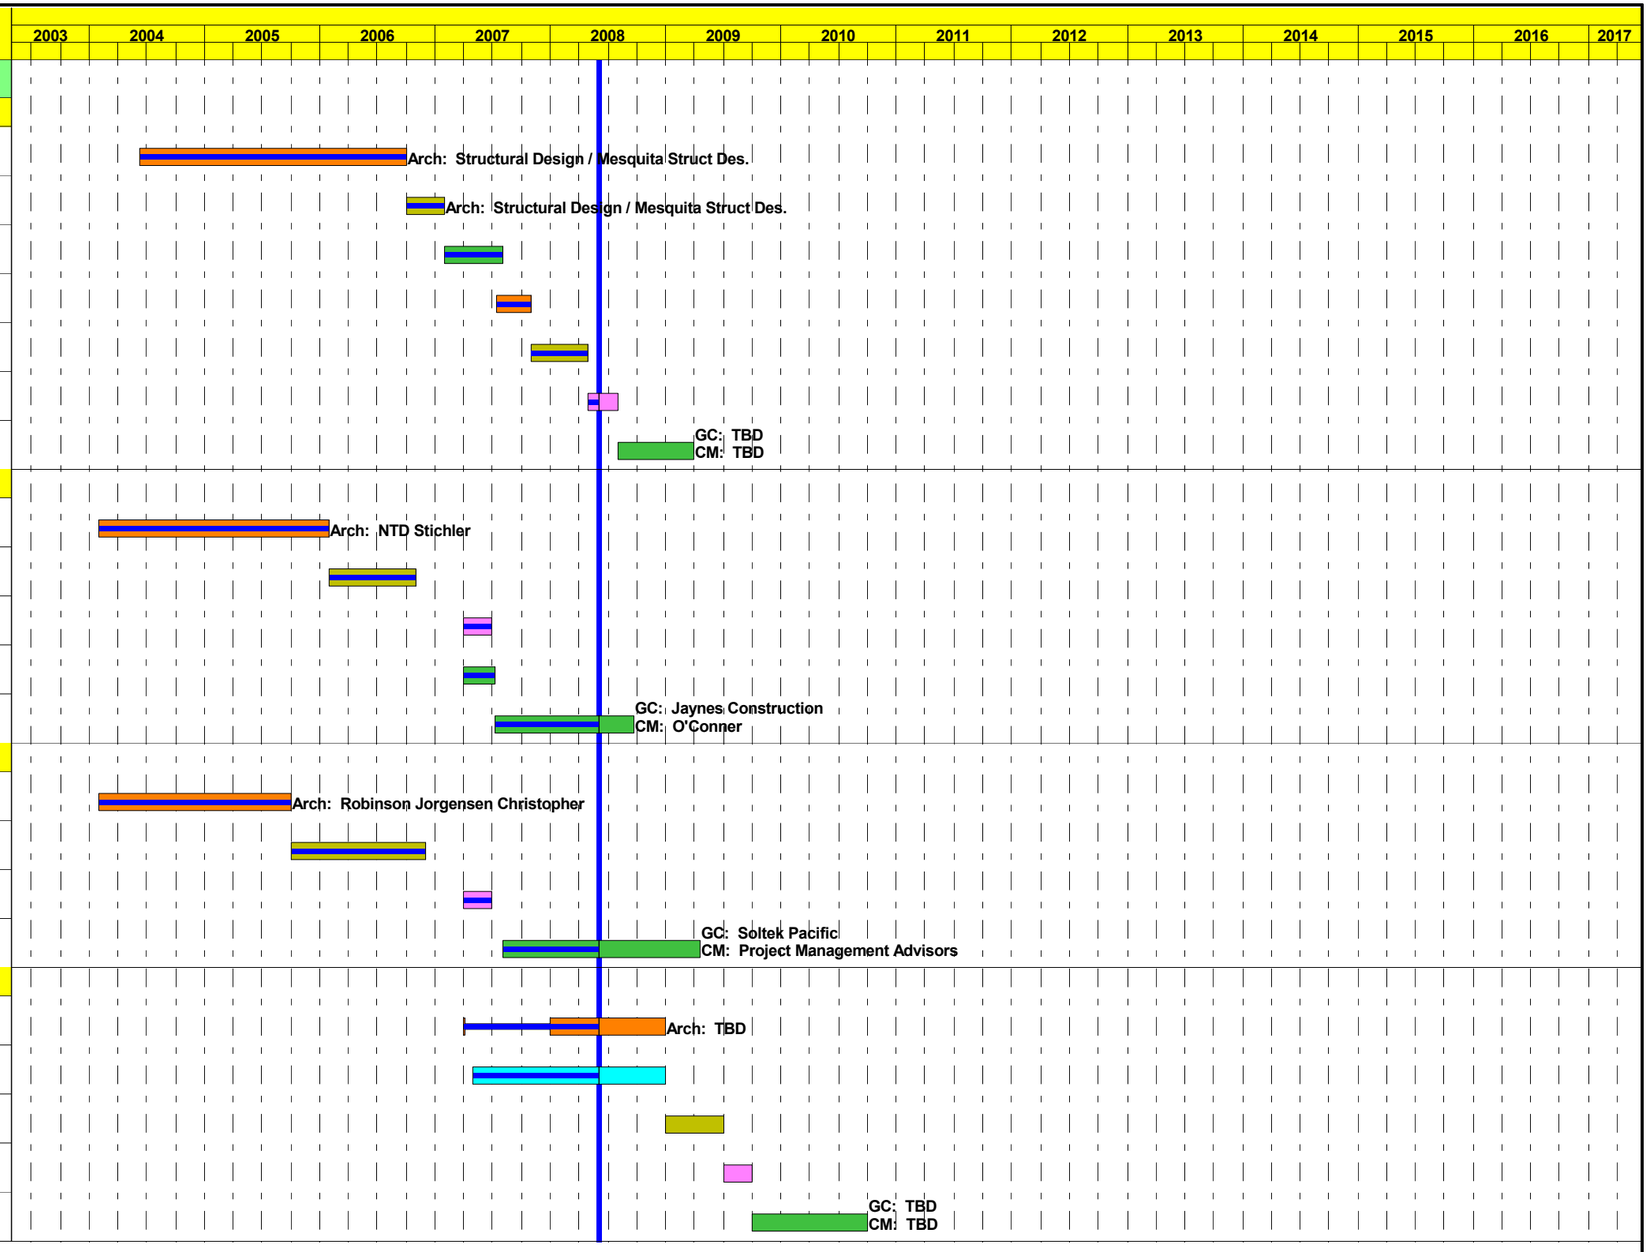

Layout: Proposition, Campus & Project
Sheet 12 of 13
Last Update: 06/01/08

© Primavera Systems, Inc.

San Diego Community College District
Master Program Schedule
Proposition "S" and "N" Projects

Design
DSA
Bid & Award
Demo/Construction
Land Aquisition
Completed
District Donation
Project Budget

The schedule has been established to guide Program Progress and dates are approximate. Due to it's magnitude, the SDCCD Proposition "S" & "N" Bond Program is subject to change. The schedule will continue to be updated as the program continues.

Activity Description	Planned (Months)	Start	Finish
North City Campus			
Land Aquisitiion	26	09/01/05A	12/10/07A
Design	32	10/02/06A	05/29/09
DSA	6	06/01/09	11/30/09
Bid & Award	3	12/01/09	02/26/10
Construction	19	03/01/10	09/30/11
Cesar Chavez Center & Center City Consolidation			
Land Aquisition	44	07/01/05A	03/02/09
Design	23	01/01/07A	02/27/09
DSA	6	03/02/09	09/01/09
Bid & Award	3	09/02/09	11/30/09
Construction	14	12/01/09	01/28/11
Educational Cultural Complex - Phase IIB Wing			
Design	12	04/01/08A	03/31/09
DSA	6	04/01/09	09/28/09
Bid & Award	3	09/29/09	12/28/09
Construction	11	12/29/09	11/30/10

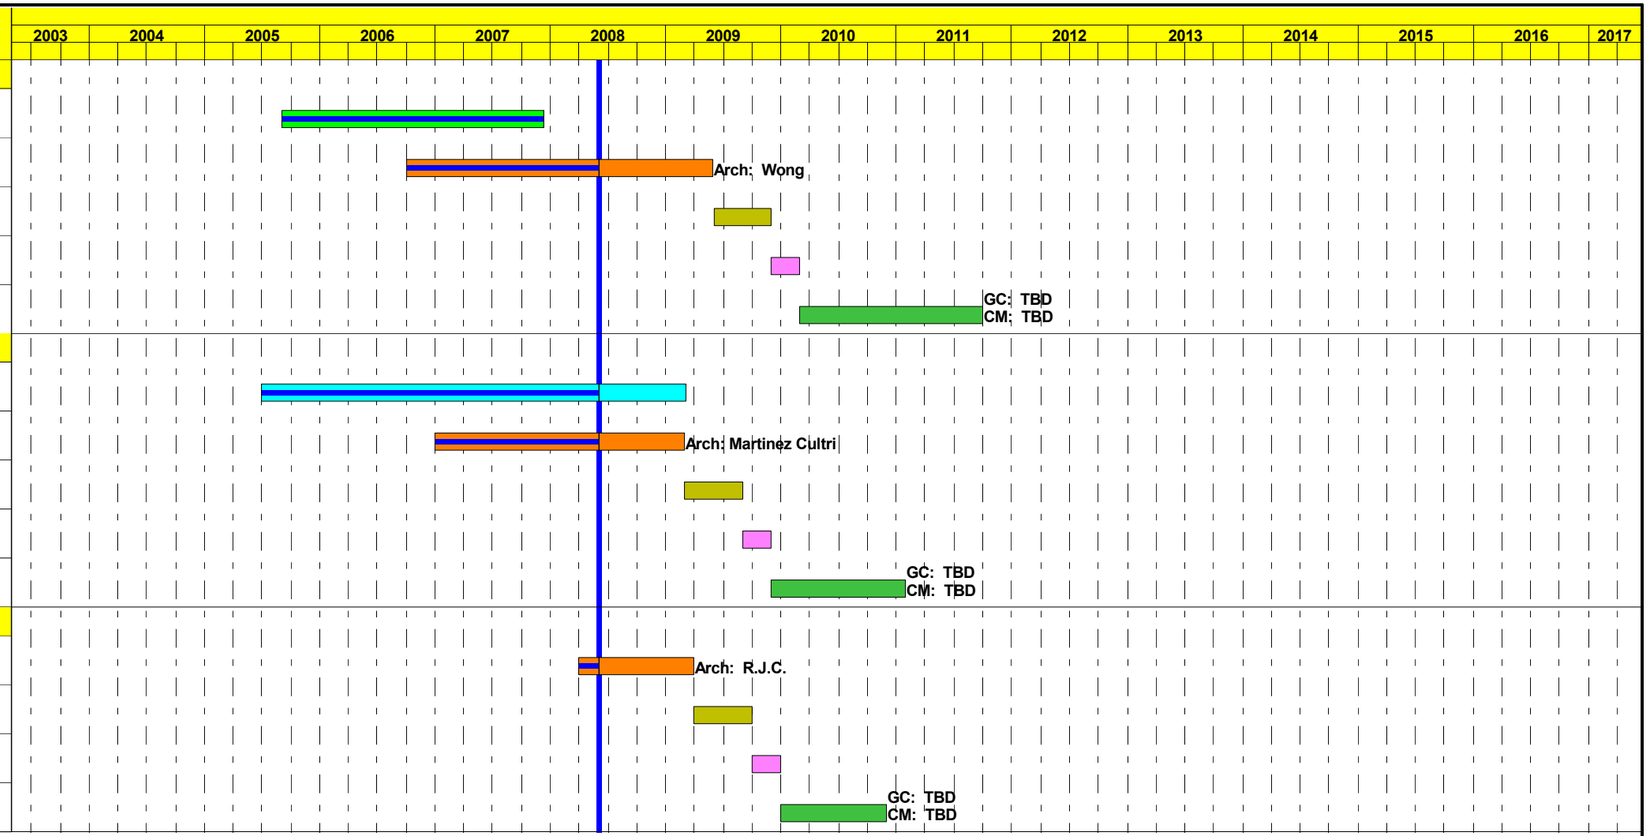

Layout: Proposition, Campus & Project
Sheet 13 of 13
Last Update: 06/01/08

© Primavera Systems, Inc.

San Diego Community College District
Master Program Schedule
Proposition "S" and "N" Projects

Design
DSA
Bid & Award
Demo/Construction
Land Aquisition
Completed
District Donation
Project Budget

The schedule has been established to guide Program Progress and dates are approximate. Due to it's magnitude, the SDCCD Proposition "S" & "N" Bond Program is subject to change. The schedule will continue to be updated as the program continues.
