Project Schedules by Campus

Activity Description	Planned (Months)	Start	Finish
San Diego Mesa College			
Campus Site Design & Env Review			
Design / Report	40	07/01/03A	11/30/06A
Renovate Visual Arts Program			
Design	9	10/03/05A	06/30/06A
DSA	4	07/06/06A	10/31/06A
Bid & Award	1	11/01/06A	11/30/06A
Construction	10	12/01/06A	09/28/07A
East Campus Improvement Project			
Land Aquisition	7	08/01/05A	02/27/06A
Design	10	08/01/05A	05/31/06A
DSA	7	06/01/06A	12/29/06A
Bid & Award	3	01/02/07A	03/30/07A
Construction Pkg (4/05/09); Pol Station 6/01/09	25	05/01/07A	06/01/09
Prepare FF&E Spec Binder	5	09/05/08A	01/30/09A
VPA Processing	1.5	02/02/09A	03/13/09
Purchasing	5	03/16/09	08/14/09
Occupancy	0		08/14/09
Temporary Parking/All Weather Track			
Design	6	07/02/07A	12/31/07A
DSA		03/23/09*	
Bid & Award Phase 1	1	10/01/07A	10/30/07A
Construction Phase 1	3	11/01/07A	02/29/08A
Bid & Award (Demolition)	2	02/02/09A	03/31/09
Construction (Demolition)	1	04/01/09*	04/30/09
Track & Field - Bid & Award	2	03/24/09*	05/14/09
Track & Field - Construction	4	05/15/09	09/15/09

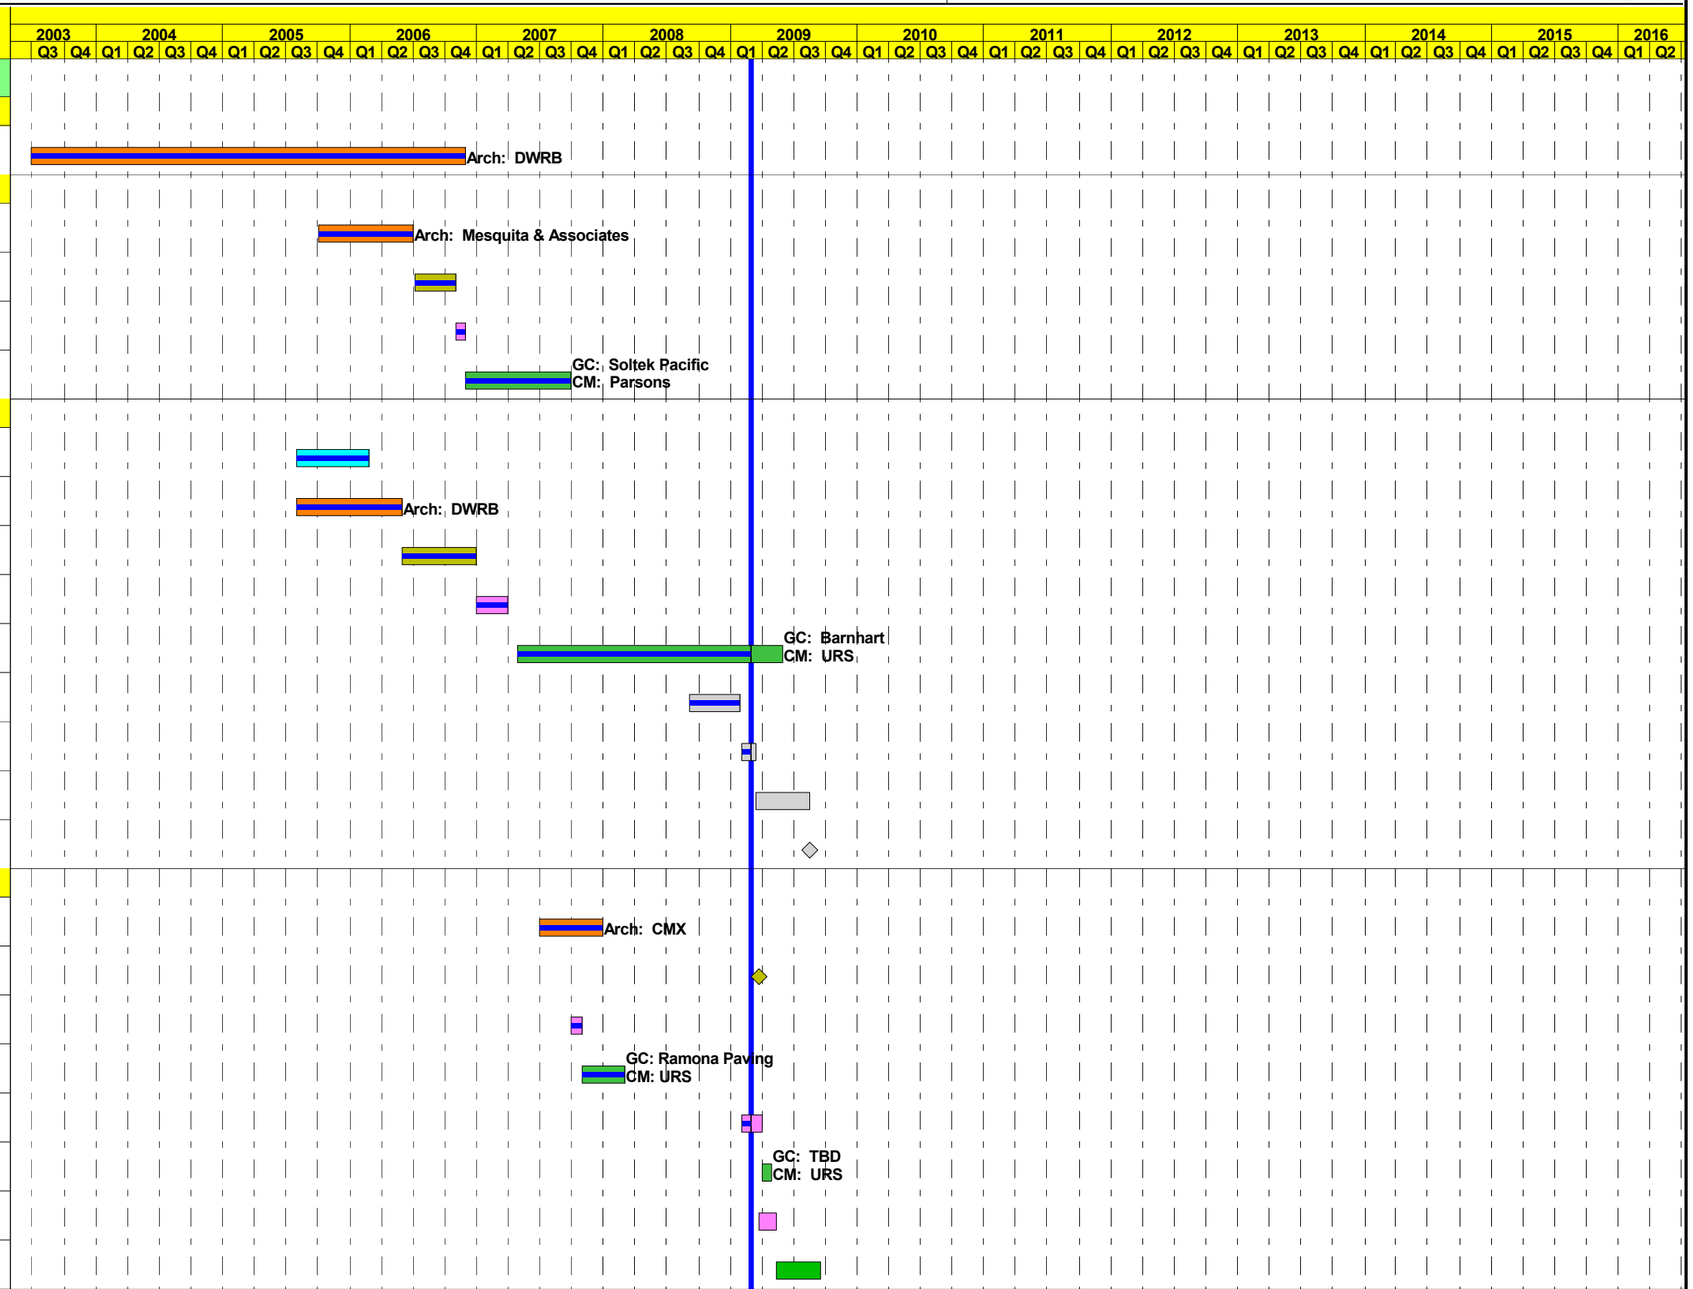

Layout: Sorted by Construction Start
Sheet 7 of 20
Last Update: 03/01/09

© Primavera Systems, Inc.

San Diego Community College District
Master Program Schedule
Proposition "S" and "N" Projects

Design
DSA
Bid & Award
Demo/Construction
FF&E
Land Aquisition
Completed
District Donation
Project Budget
Occupancy

The schedule has been established to guide Program Progress and dates are approximate. Due to it's magnitude, the SDCCD Proposition "S" & "N" Bond Program is subject to change. The schedule will continue to be updated as the program continues.

Project Schedules by Campus

Activity Description	Planned (Months)	Start	Finish
Allied Health Building			
Design	36	08/02/04A	08/06/07A
DSA	5	08/08/07A	12/31/07A
Bid & Award	2	03/03/08A	05/09/08A
Construction	15.5	05/12/08A	08/31/09
Prepare FF&E Spec Binder	7	07/15/08A	02/25/09A
VPA Processing	1	03/02/09	03/25/09
Purchasing	3	03/26/09	06/15/09
Occupancy	0		06/15/09
Modular Village			
Design	6	09/01/08A	02/27/09A
DSA	1d	03/02/09*	03/02/09
Bid & Award	1.5	03/10/09*	04/16/09
Construction	5	04/17/09	09/15/09
Muir Renovation			
Design	5	04/01/08A	08/29/08A
DSA	8	09/01/08A	04/30/09
Bid & Award	3	05/01/09	07/31/09
Construction	6	08/03/09	01/29/10
Student Services Facility			
Design	32	07/03/06A	02/27/09A
DSA	4	02/02/09A	05/29/09
Bid & Award	3	06/01/09*	08/31/09
Demolition	3	09/01/09	11/30/09
Construction	14	12/01/09*	02/01/11
Prepare FF&E Spec Binder	5	02/26/10*	07/29/10
VPA Processing	2	07/30/10	09/30/10
Purchasing	6	10/01/10	04/01/11
Occupancy	0		06/01/11*

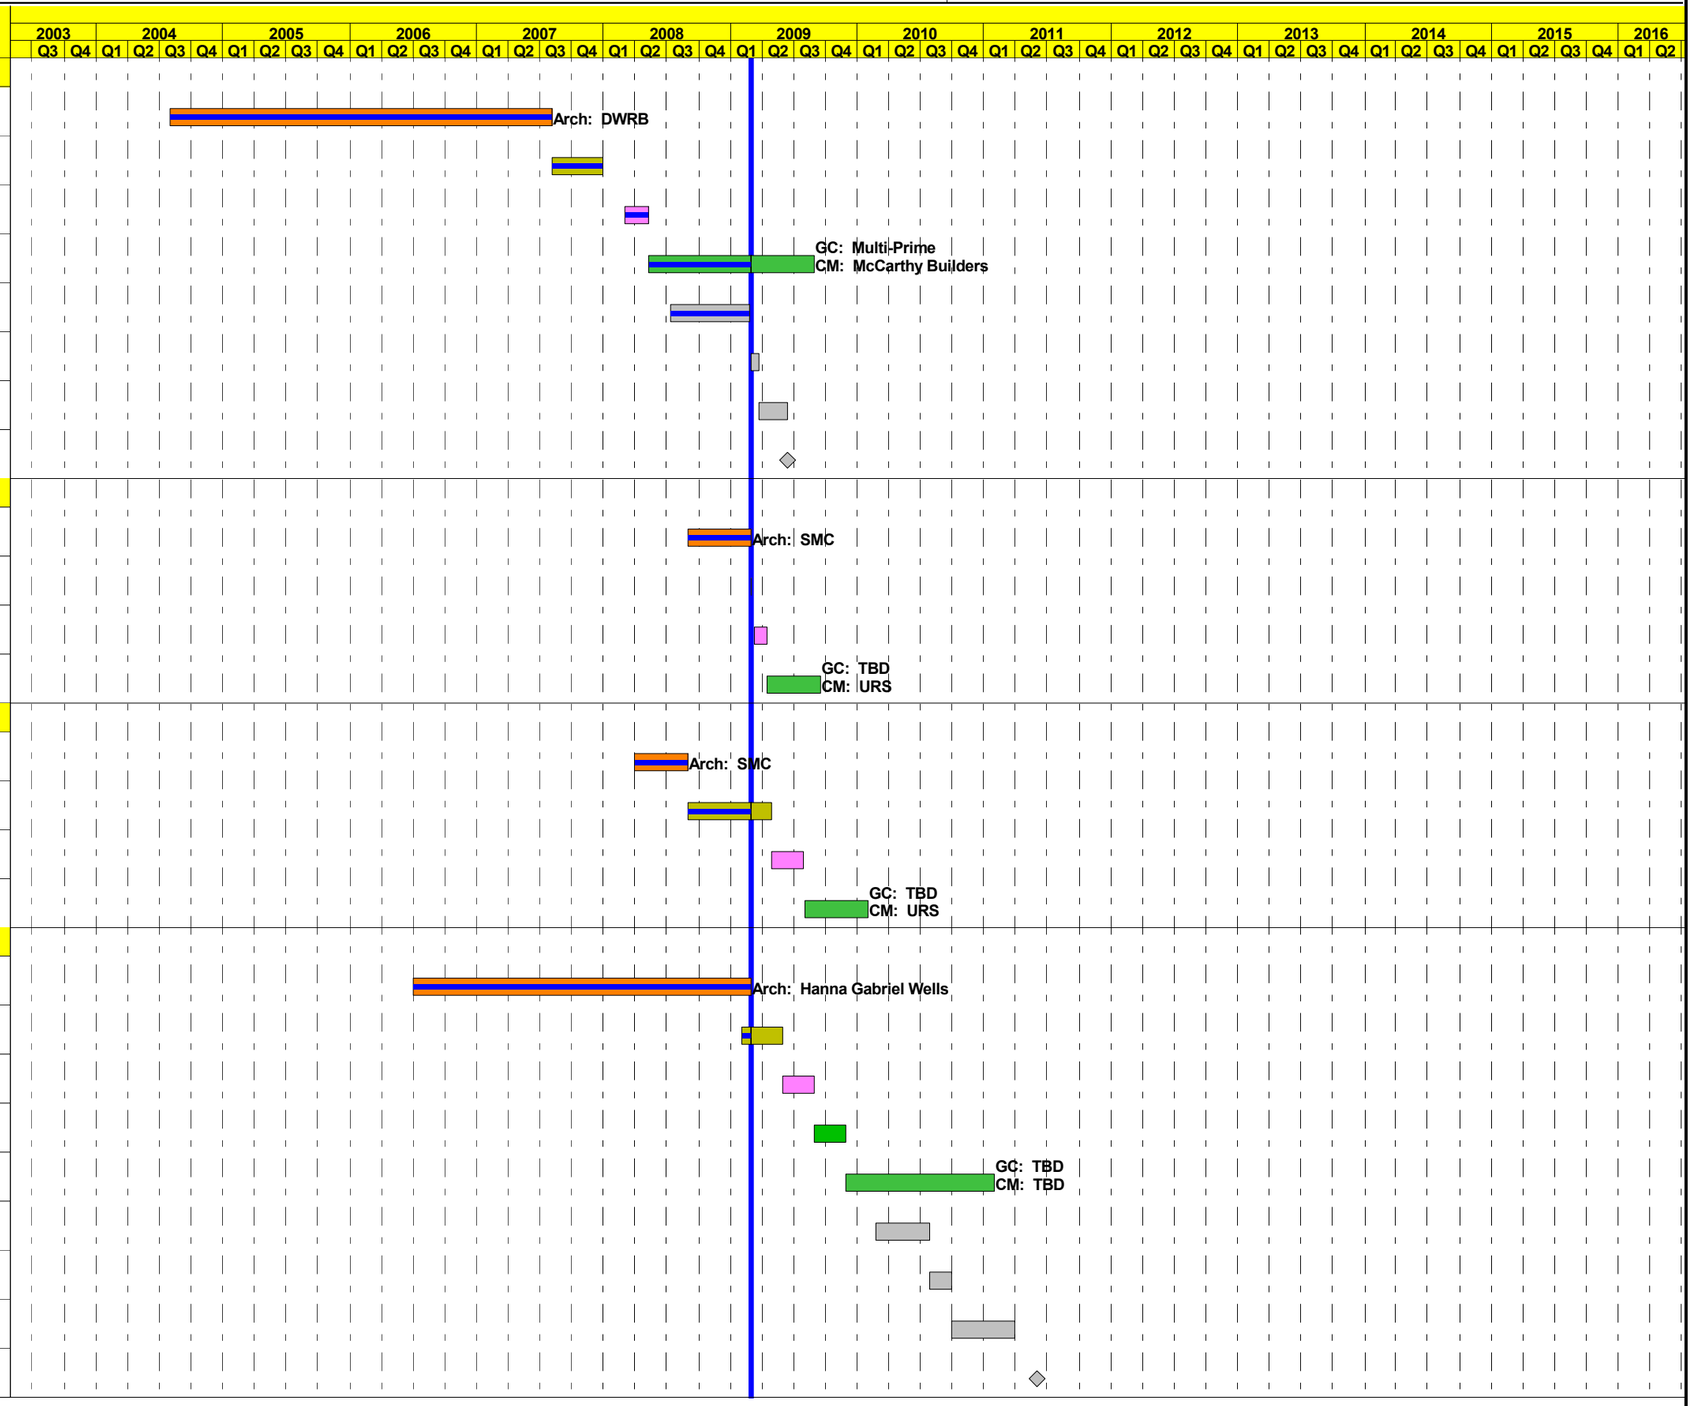

Layout: Sorted by Construction Start
Sheet 8 of 20
Last Update: 03/01/09

© Primavera Systems, Inc.

San Diego Community College District
Master Program Schedule
Proposition "S" and "N" Projects

Design
DSA
Bid & Award
Demo/Construction
FF&E
Land Aquisition
Completed
District Donation
Project Budget
Occupancy

The schedule has been established to guide Program Progress and dates are approximate. Due to it's magnitude, the SDCCD Proposition "S" & "N" Bond Program is subject to change. The schedule will continue to be updated as the program continues.

Project Schedules by Campus

Activity Description	Planned (Months)	Start	Finish
Infrastructure - Fire/Utilities/etc			
Design	12	06/02/08A	05/29/09
DSA	6	06/01/09	11/30/09
Bid & Award	3	12/01/09	03/01/10
Construction	39	04/01/10*	06/28/13
Math and Science Building			
Design	17	06/02/08A	10/30/09
DSA	7	11/02/09*	05/31/10
Bid & Award	3	06/01/10	08/27/10
Demolition	3	06/02/10	09/01/10
Construction	24	09/02/10*	08/31/12
Prepare FF&E Spec Binder	5	05/02/11*	09/30/11
VPA Processing	2	01/02/12*	02/29/12
Purchasing	6	03/01/12	09/03/12
Occupancy	0		09/03/12
Social Behavioral Science			
Design	12	09/01/10*	08/31/11
DSA	6	09/01/11*	02/29/12
Bid & Award	3	03/01/12*	05/31/12
Construction	21	09/03/12*	05/30/14
Prepare FF&E Spec Binder	5	05/01/13*	09/30/13
VPA Processing	2	01/01/14*	02/28/14
Purchasing	7	03/03/14	08/22/14
Occupancy	0		08/22/14

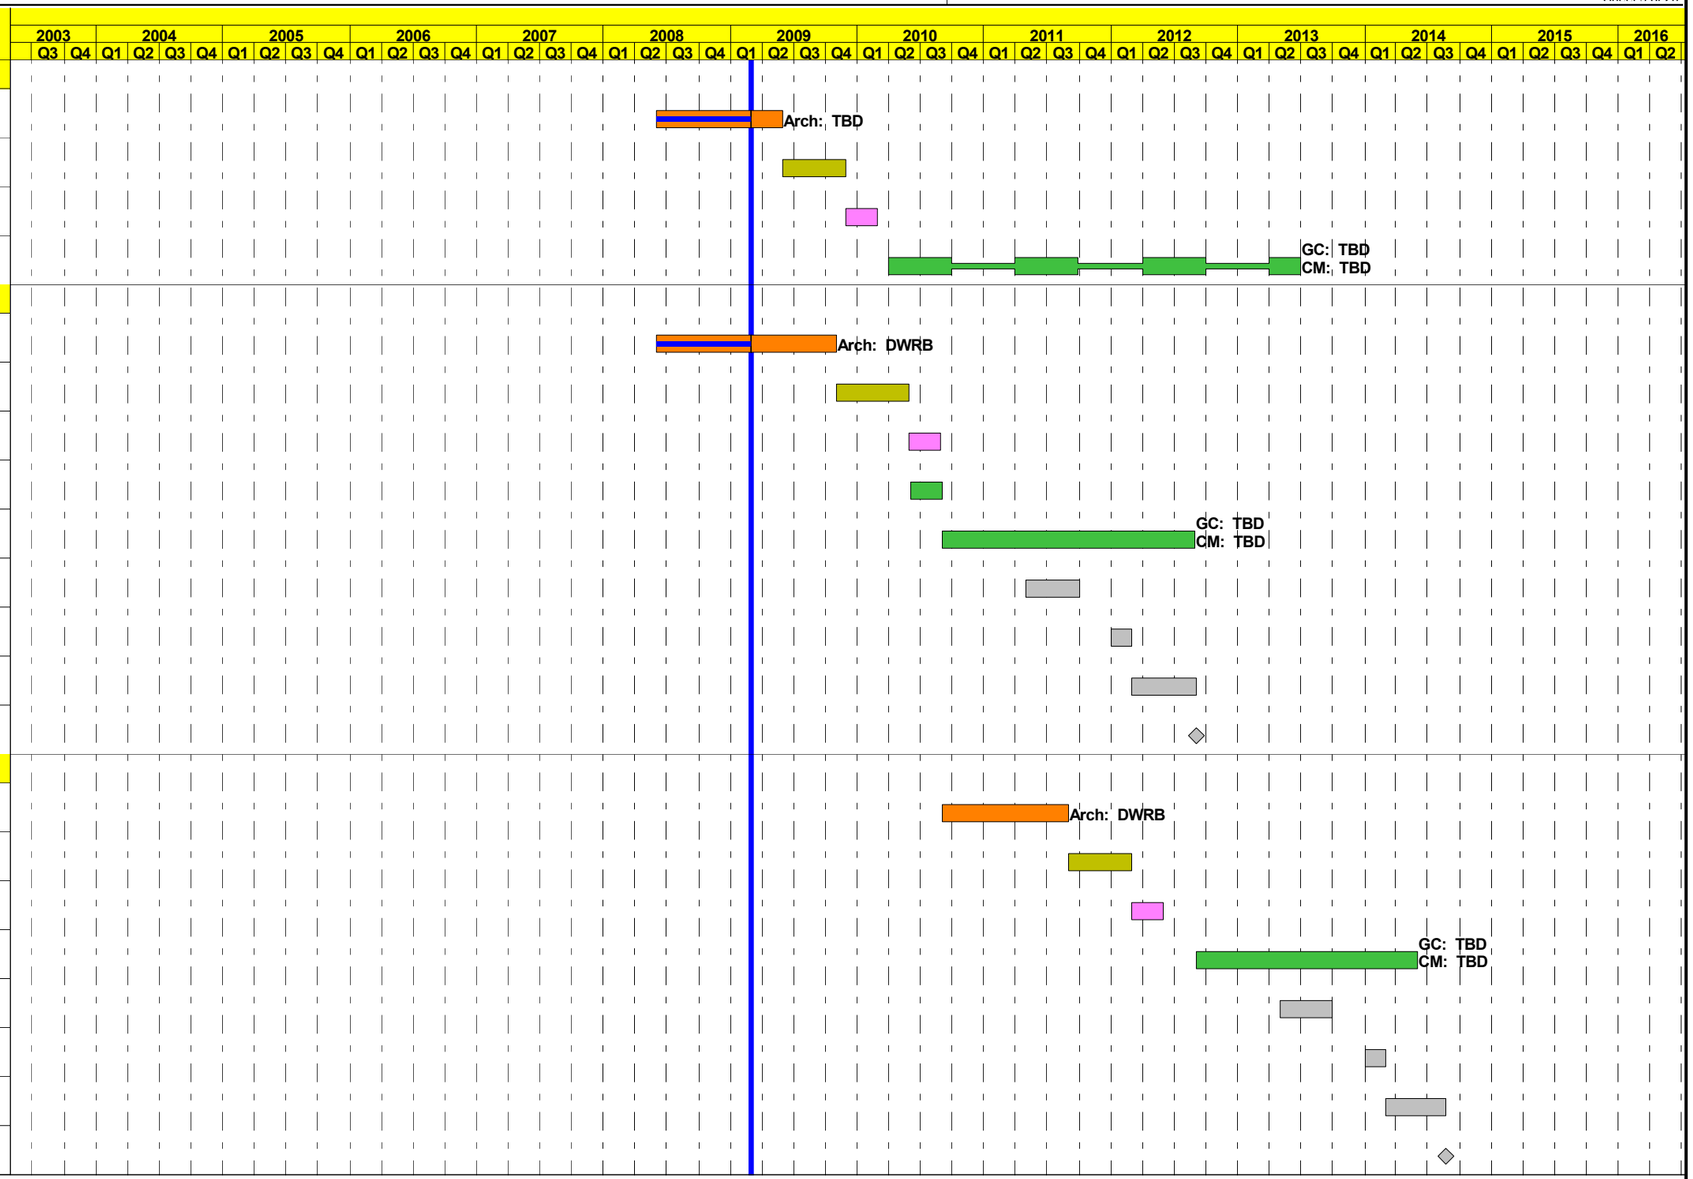

Layout: Sorted by Construction Start
Sheet 9 of 20
Last Update: 03/01/09

© Primavera Systems, Inc.

San Diego Community College District
Master Program Schedule
Proposition "S" and "N" Projects

- Design
- DSA
- Bid & Award
- Demo/Construction
- FF&E
- Land Aquisition
- Completed
- District Donation
- Project Budget
- Occupancy

The schedule has been established to guide Program Progress and dates are approximate. Due to it's magnitude, the SDCCD Proposition "S" & "N" Bond Program is subject to change. The schedule will continue to be updated as the program continues.

Project Schedules by Campus

Activity Description	Planned (Months)	Start	Finish
Fitness Center			
Design	12	09/15/10*	09/14/11
DSA	6	09/15/11*	03/14/12
Bid & Award	3	03/15/12*	06/15/12
Construction	19	09/03/12*	03/31/14
Prepare FF&E Spec Binder	5	02/01/13*	07/02/13
VPA Processing	2	09/16/13*	11/18/13
Purchasing	9	11/19/13	08/22/14
Occupancy	0		08/22/14
Instructional Technology Building			
Design	14	03/01/12*	04/30/13
DSA	7	05/01/13*	11/29/13
Bid & Award	3	12/02/13	02/28/14
Construction	18	03/03/14	08/31/15
Prepare FF&E Spec Binder	5	04/30/14*	09/30/14
VPA Processing	2	01/01/15*	02/27/15
Purchasing	6	03/02/15*	08/31/15
Occupancy	0		08/31/15
Stockroom & Campus Facilities Support Areas			
Design	12	05/01/12*	04/30/13
DSA	6	05/01/13	10/31/13
Bid & Award	4	11/01/13	02/28/14
Construction	12	03/03/14	03/02/15
Prepare FF&E Spec Binder	5	11/01/13*	03/31/14
VPA Processing	2	06/30/14*	09/01/14
Purchasing	6	09/02/14*	02/27/15
Occupancy	0		02/27/15

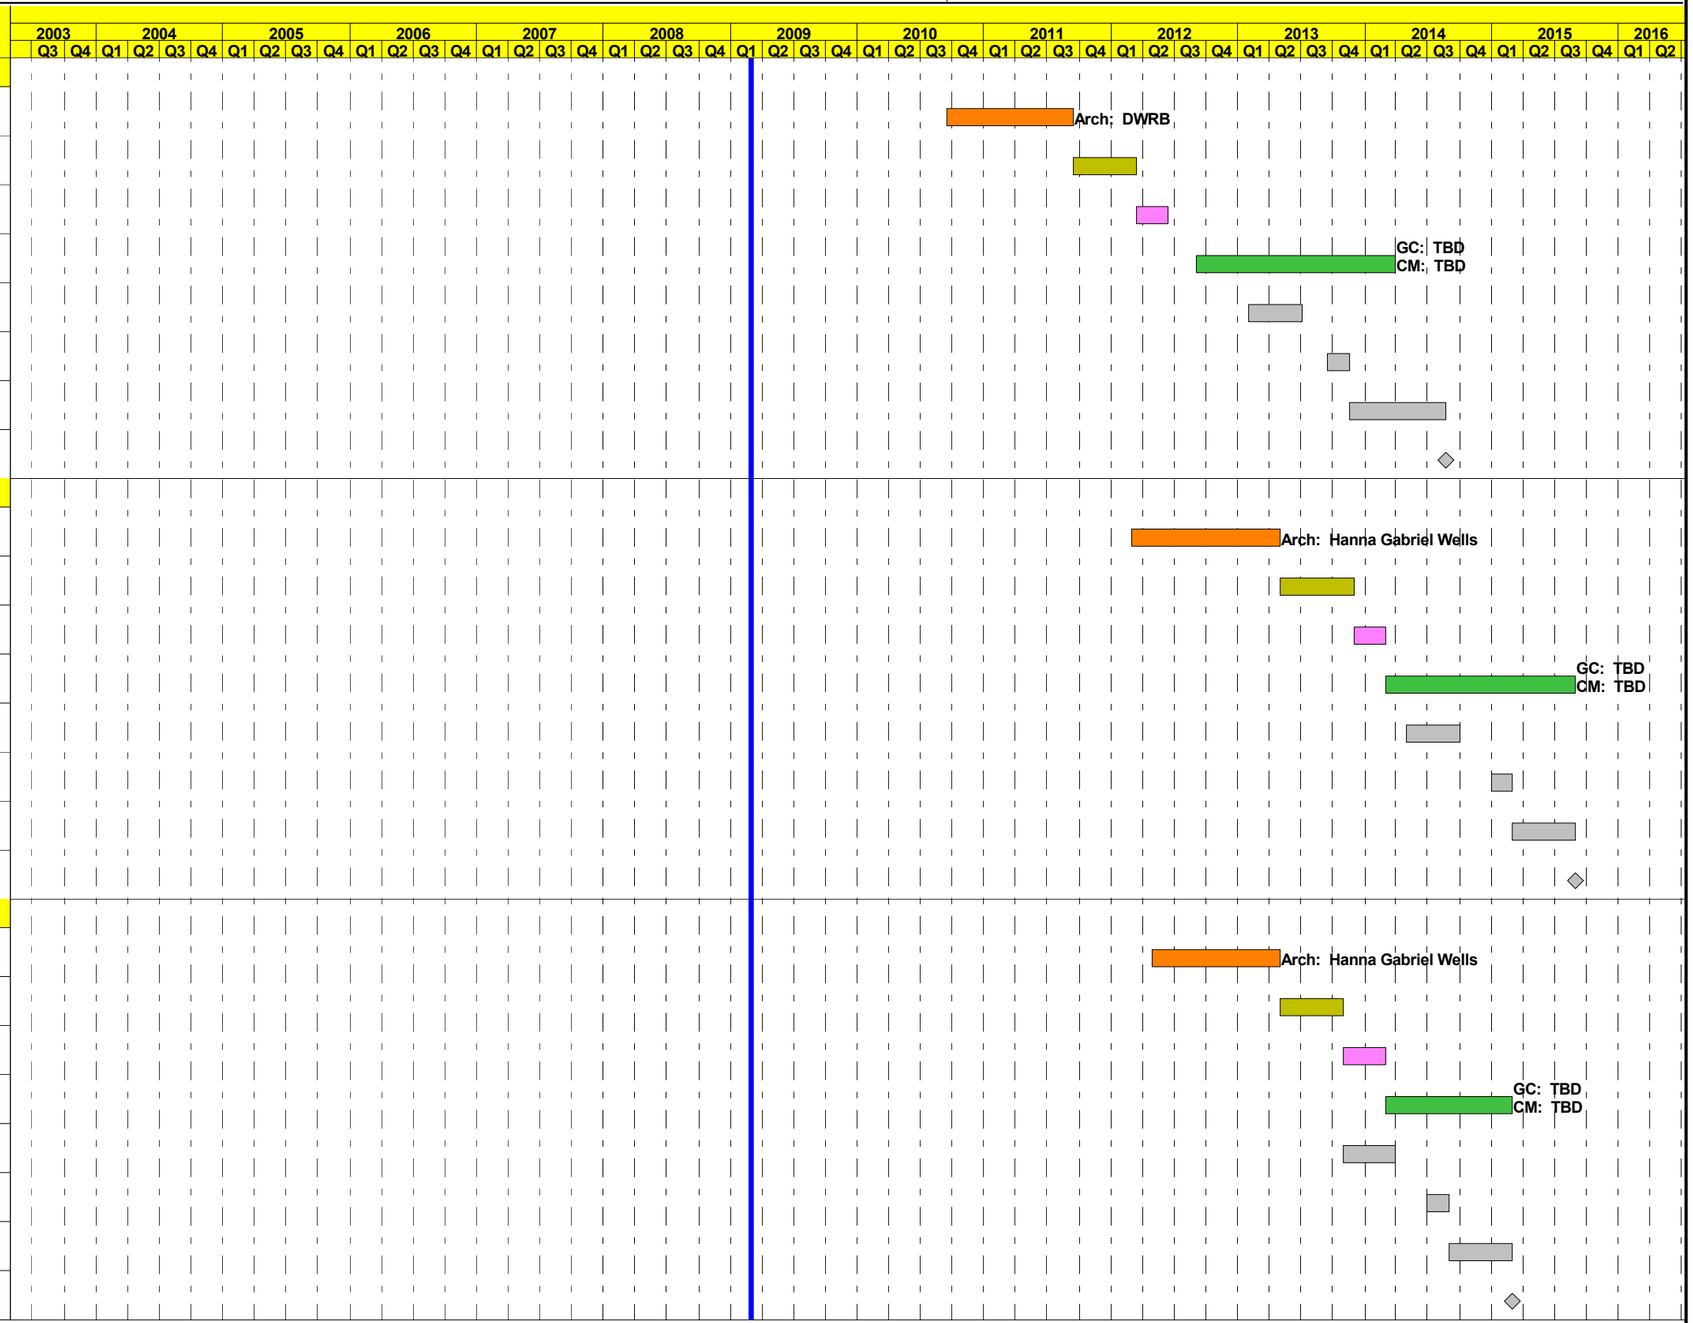

Layout: Sorted by Construction Start
Sheet 10 of 20
Last Update: 03/01/09

© Primavera Systems, Inc.

San Diego Community College District
Master Program Schedule
Proposition "S" and "N" Projects

Design
DSA
Bid & Award
Demo/Construction
FF&E
Land Aquisition
Completed
District Donation
Project Budget
Occupancy

The schedule has been established to guide Program Progress and dates are approximate. Due to it's magnitude, the SDCCD Proposition "S" & "N" Bond Program is subject to change. The schedule will continue to be updated as the program continues.

Project Schedules by Campus

Activity Description	Planned (Months)	Start	Finish
Cafeteria and Bookstore			
Design	12	09/01/10*	08/31/11
DSA	6	09/01/11	02/29/12
Bid & Award	6	03/01/12	08/31/12
Construction	19	09/03/12	03/31/14
Prepare FF&E Spec Binder	5	11/30/12*	04/30/13
VPA Processing	2	08/01/13*	09/30/13
Purchasing	11	10/01/13	08/29/14
Occupancy	0		08/29/14
Fine Arts and Dramatic Arts Curriculum			
Design	12	05/01/12*	04/30/13
DSA	6	05/01/13	10/31/13
Bid & Award	3	12/02/13*	02/28/14
Construction	12	03/03/14	02/27/15
Prepare FF&E Spec Binder	5	10/31/13*	03/31/14
VPA Processing	2	06/30/14*	09/01/14
Purchasing	5	09/02/14	02/06/15
Occupancy	0		02/06/15
I - 300 Building Renovatiom			
Design	12	08/15/11*	08/14/12
DSA	6	08/15/12*	02/15/13
Bid & Award	3	02/18/13*	05/16/13
Construction	12	05/17/13*	05/16/14
Prepare FF&E Spec Binder	5	02/01/13*	07/02/13
VPA Processing	2	10/01/13*	12/03/13
Purchasing	6	12/04/13	06/02/14
Occupancy	0		06/02/14

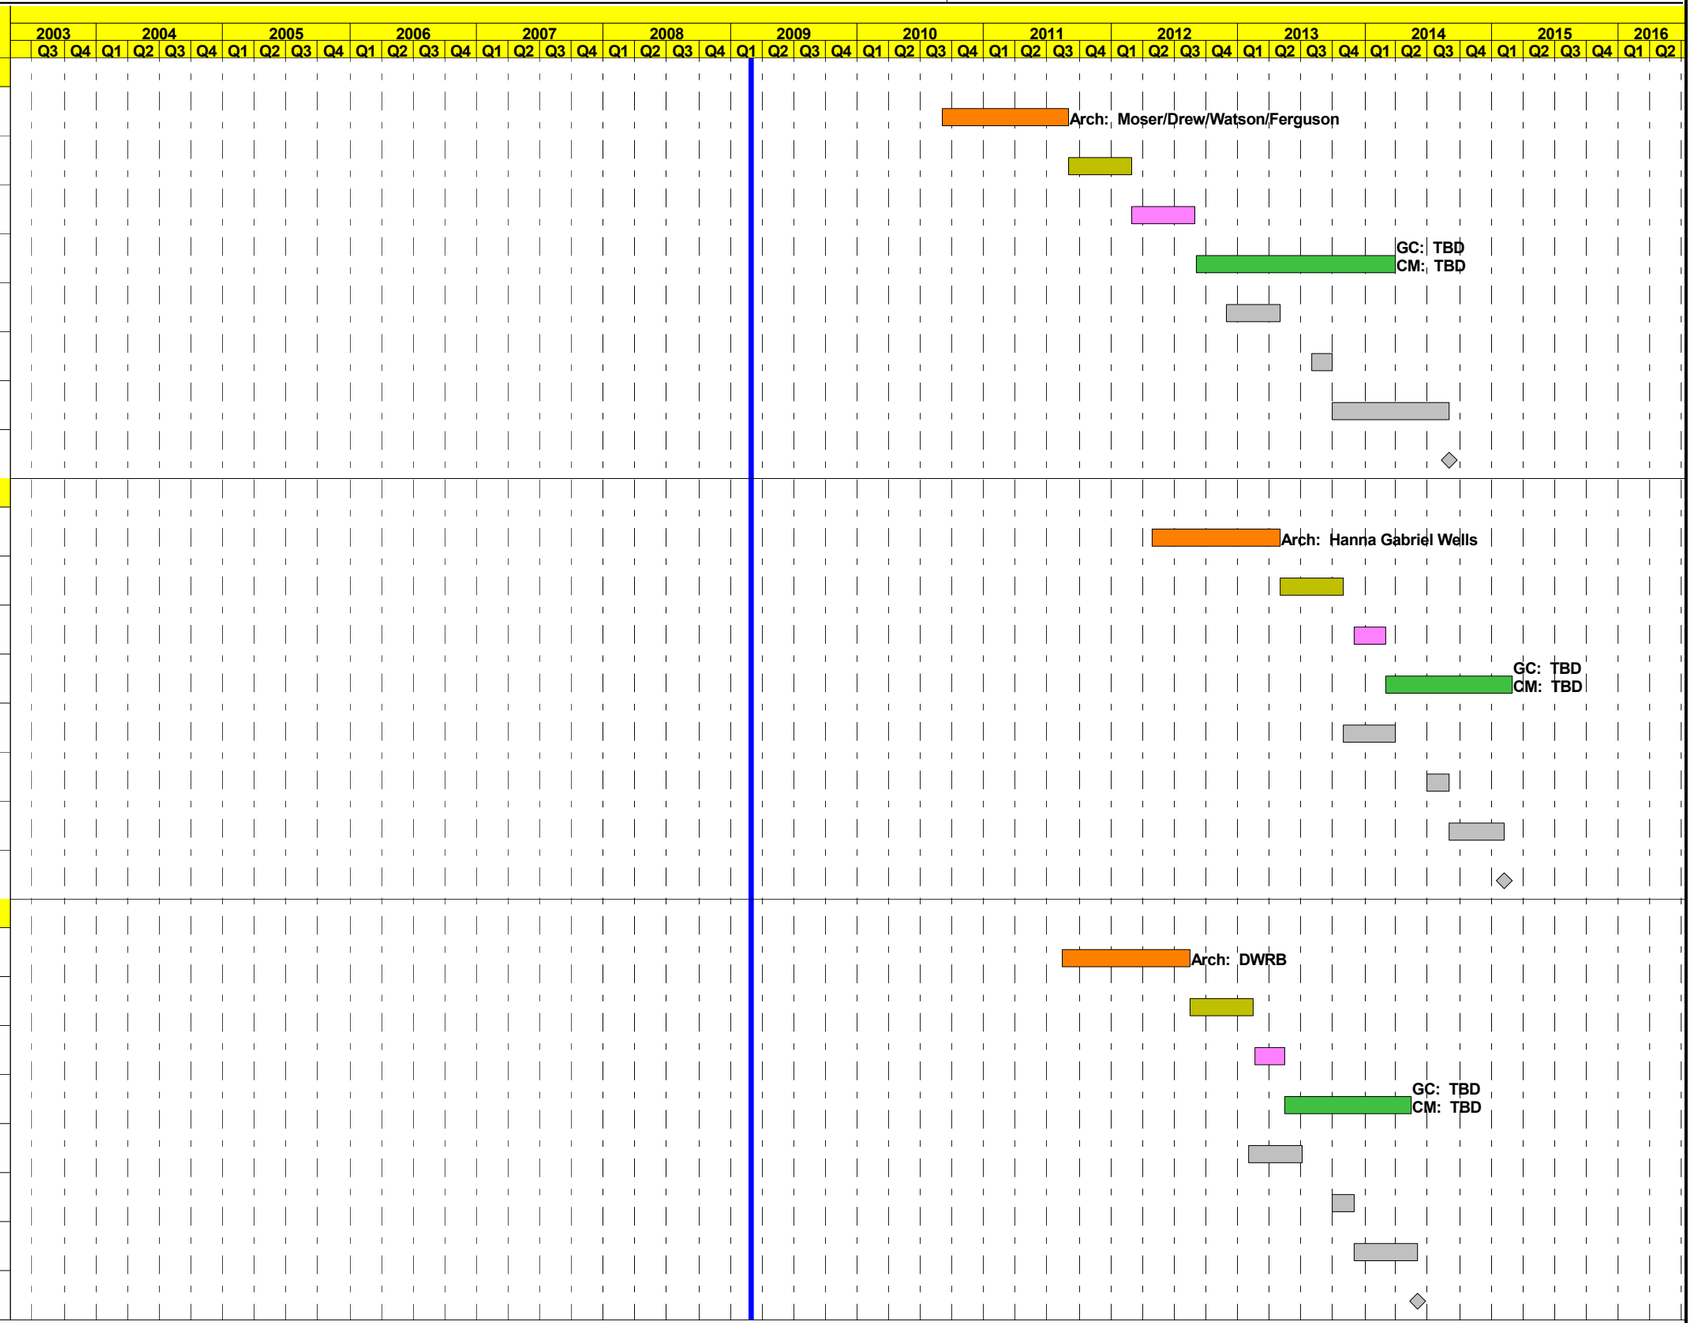

Layout: Sorted by Construction Start
Sheet 11 of 20
Last Update: 03/01/09

© Primavera Systems, Inc.

San Diego Community College District
Master Program Schedule
Proposition "S" and "N" Projects

Design
DSA
Bid & Award
Demo/Construction
FF&E
Land Aquisition
Completed
District Donation
Project Budget
Occupancy

The schedule has been established to guide Program Progress and dates are approximate. Due to it's magnitude, the SDCCD Proposition "S" & "N" Bond Program is subject to change. The schedule will continue to be updated as the program continues.
